

Name: Tejas Shetty

SRN: PES1UG24AM305

SE LAB 2

SPRINT1:

In progress:

The screenshot shows a Jira board for the 'AEBAS board' (Academic Elective Bidding & Allocation System). The board is in a sprint state, with a 'Complete sprint' button visible. The board is organized into four columns: TO DO (3 items), IN PROGRESS (2 items), IN REVIEW (1 item), and DONE (1 item). Each item is a story card with a title, description, and metadata.

Column	Count	Story Title	EPIC	Key	Priority	Assignee
TO DO	3	Story 2.2: Distribute 100 Bidding Credits	EPIC 2: Student Bidding & Credit Distr...	AEBAS-10	5	
		Story 2.3: Validate Prerequisite Completion	EPIC 2: Student Bidding & Credit Distr...	AEBAS-11	5	
		Story 2.4: Lock Bid and Issue Reference Number	EPIC 2: Student Bidding & Credit Distr...			
IN PROGRESS	2	Story 1.2: Configure Seat Capacity	EPIC 1: Bidding Window & Course Co...	AEBAS-7	3	
		Story 2.1: Rank Elective Preferences	EPIC 2: Student Bidding & Credit Distr...	AEBAS-9	3	
IN REVIEW	1	Story 1.3: View Published Elective Catalog	EPIC 1: Bidding Window & Course Co...	AEBAS-8	3	
DONE	1	Story 1.1: Configure Bidding Window	EPIC 1: Bidding Window & Course Co...	AEBAS-6	5	

Completed:

Spaces / Academic Elective Bidding & Allocation System

AEBAS board


Summary List **Active sprints** Backlog Development Forms Timeline Docs Reports +

Search board Version Epic Label Quick filters Complete sprint Group: Story


TO DO	IN PROGRESS	IN REVIEW	DONE 7
			REFERENCE NUMBER EPIC 2: Student Bidding & Credit Distr... AEBAS-12 3 Story 1.3: View Published Elective Catalog EPIC 1: Bidding Window & Course Co... AEBAS-8 3 Story 2.3: Validate Prerequisite Completion EPIC 2: Student Bidding & Credit Distr... AEBAS-11 5

SPRINT2:

In Progress:

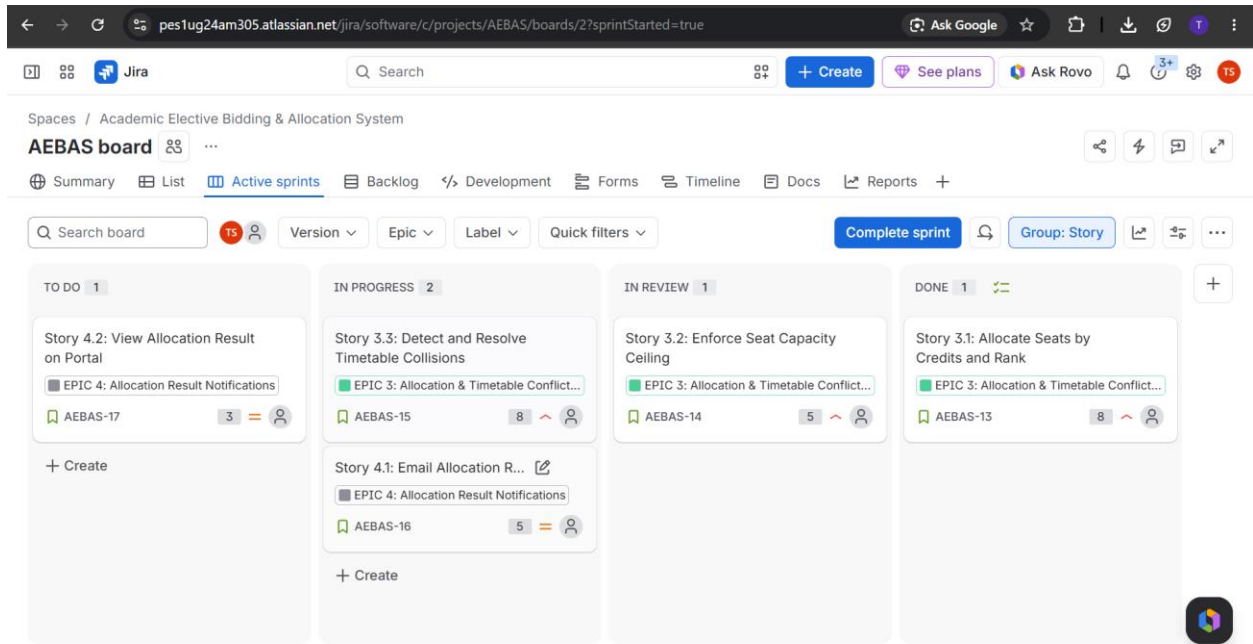


Completed:

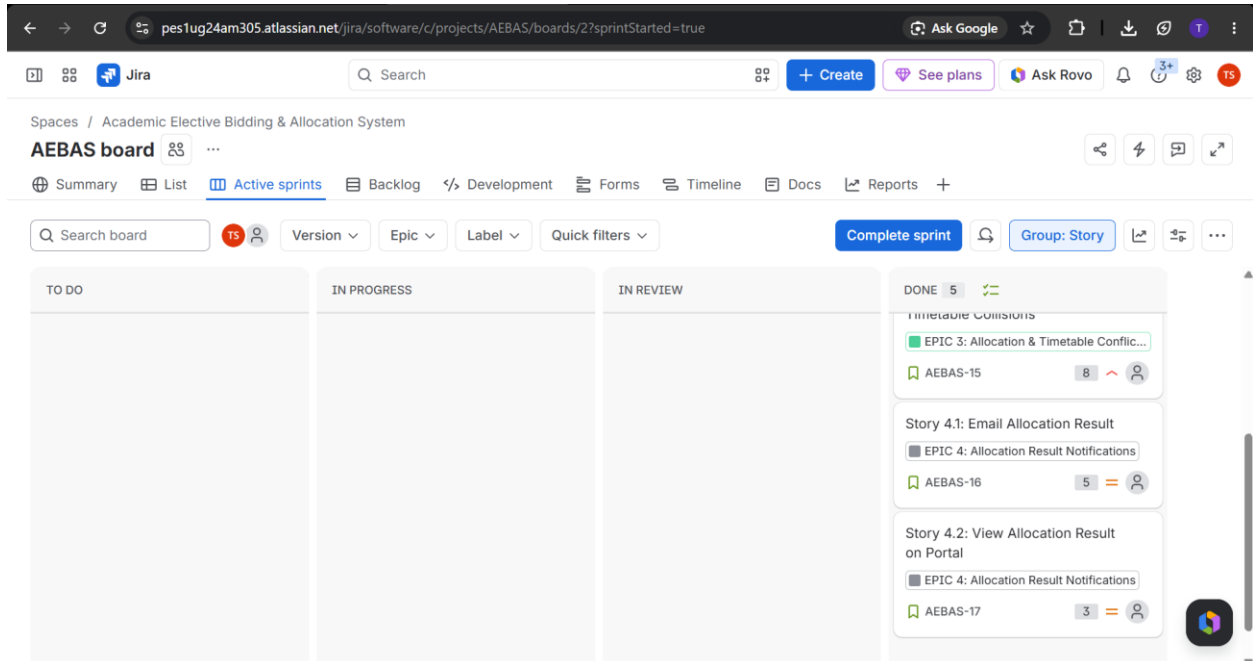


BURNDOWN CHARTS

SPRINT1

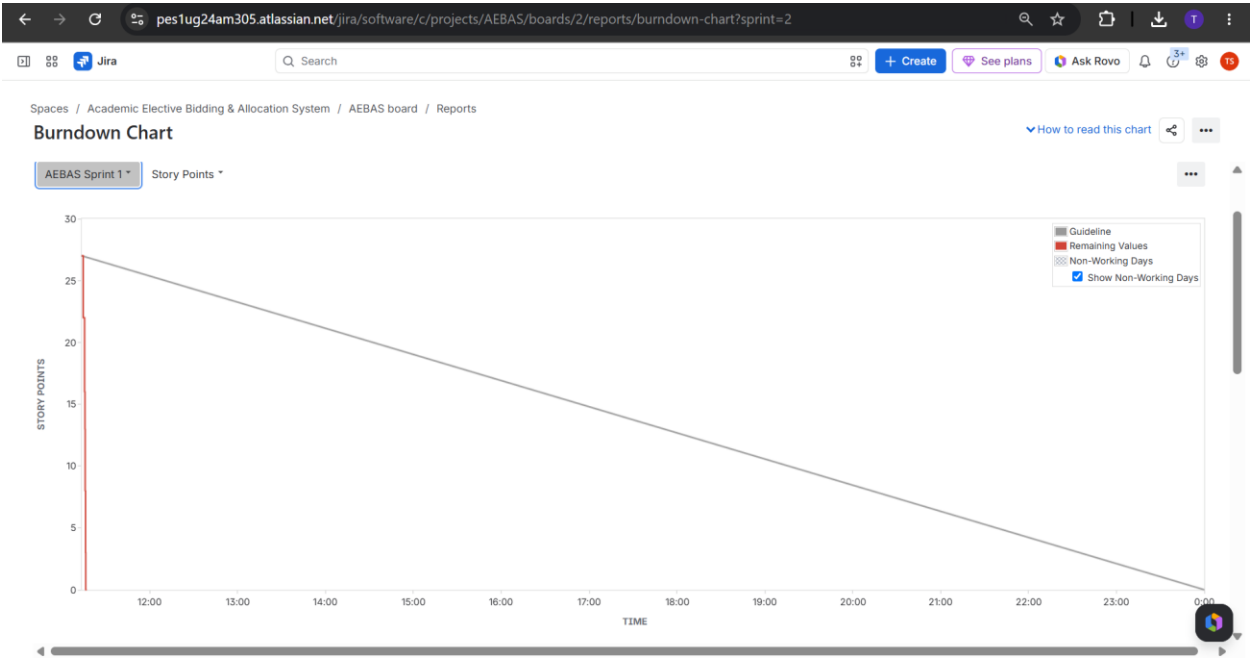

SPRINT2

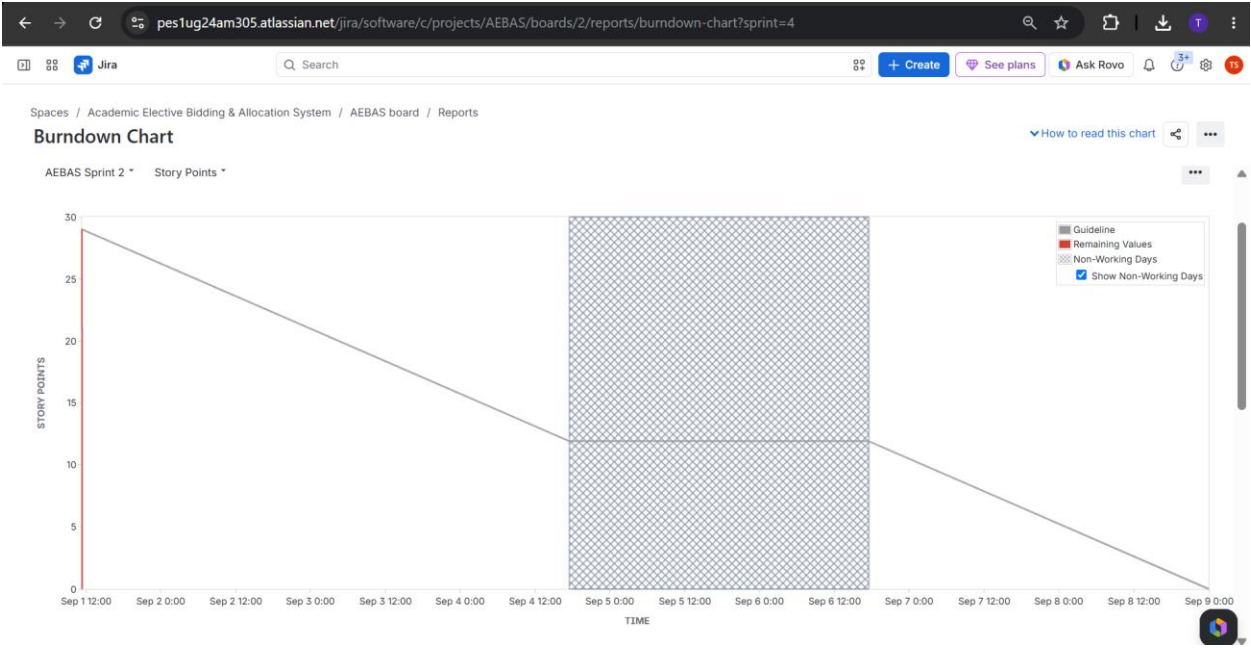

REFLECTION QUESTIONS

1. Did your estimations reflect the actual effort?

The relative sizing was reasonable. Configuration and display stories were estimated low: Configure Seat Capacity, View Published Elective Catalog and View Allocation Result on Portal were 3 points each. Stories with real logic or validation were estimated higher: Configure Bidding Window, Distribute 100 Bidding Credits, Validate Prerequisite Completion and Enforce Seat Capacity Ceiling were 5 points each. The two hardest stories, Allocate Seats by Credits and Rank and Detect and Resolve Timetable Collisions, were given 8 points because they carry the most uncertainty, such as tie-breaking between equal bids, seat overflow and clashing time slots. The Fibonacci scale forced a clear jump to 8 rather than an in-between guess.

Because the sprints were simulated, these estimates were never tested against real development effort. Looking back, Story 3.3 bundles two jobs, detecting collisions and resolving them, and should probably have been split into two stories. An 8-point story with "and" in its title is a common sign of hidden work.

2. Was your backlog well-prioritized?

The order followed the system's natural dependency chain. Epic 1 (Bidding Window & Course Configuration) and Epic 2 (Student Bidding & Credit Distribution) went into Sprint 1, because students cannot bid until the bidding window and seat capacities exist. Epic 3 (Allocation & Timetable Conflict) and Epic 4 (Allocation Result Notifications) went into Sprint 2, because allocation needs locked bids and notifications need allocation results. Marking the notification stories as Medium was correct, since the system still works without emails.

The weakness is that 9 of the 12 stories are High priority. When almost everything is High, the priority field stops helping decide what to do first. Also, View Published Elective Catalog was marked Medium, but students cannot make informed bids without seeing the catalog, so it arguably should have been High.

3. How did your simulated sprint align with your plan?

Both sprints fully matched the plan. Sprint 1 committed 7 stories (27 story points) and completed all 7. Sprint 2 committed 5 stories (29 story points) and completed all 5. Nothing carried over to the next sprint. The board snapshots show work flowing roughly in story order: in Sprint 1, Story 1.1 reached Done first while 1.2 and 2.1 were In Progress, 1.3 was In Review, and the remaining Epic 2 stories were still in To Do. Adding an In Review column made the workflow more realistic than the default three columns, because a story is not Done until it has been checked.

However, the perfect match is a result of the simulation, not proof of accurate planning. There were no blockers, defects or scope changes. In a real sprint, the two 8-point allocation stories would be the most likely to slip.

4. What insights did the burndown chart give about your team's capacity?

In both charts, the red Remaining Values line drops almost straight to zero right after the sprint starts, far below the grey guideline. This happened because all stories were moved to Done within minutes. A sharp drop like this usually means work was not broken down well or the board was not updated as work happened; here it is simply because the sprint was simulated, so the charts do not show a real burn rate. The Sprint 2 chart does show one realistic feature: the guideline flattens over the shaded non-working days (5-6 September), because Jira does not expect progress on weekends.

In terms of capacity, the two sprints give a velocity of 27 and 29 points, an average of about 28 points per sprint. That is a reasonable starting commitment for Sprint 3, but it should be treated as a planning assumption until real sprints, with daily board updates, produce a burndown that actually tracks the guideline.
